

BAR UPGRADE 2015 / 2016

Completed Feb 2016



BEFORE




TAKING THE BAR APART



WALL'S ALL DOWN / NEW BAR PARTS



DAY 2.5 TAKING SHAPE

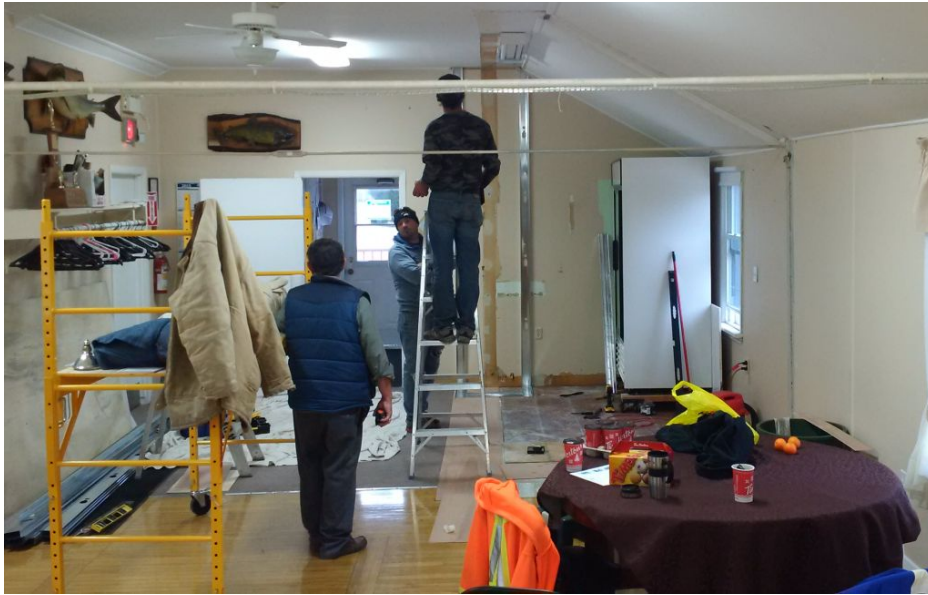

DAY 3.5 CONSTRUCTION CONTINUES



DAY 4.5 WORK CONTINUES

Dec 30, 2015 - No PIC's - No Visible Changes - Working on Various Background items before new bar furniture installation

=====



Dec 31, 2015 Day 5.5 Work Continues



Installing lift Section



First Section Placement



Second Section in Place

Plumbing Started, Lighting / Power,
More Dry Wall mud, More Planning


JAN 01, 2016 === DAY 6.5 WORK CONTINUES



No real visual changes Today Lots of background work

JAN 02, 2016 DAY 7.5 WORK CONTINUES

**Likely no PIC's today,
Trim & Moulding up, Stan
worked on the bar, more dry
wall sanding etc etc
small things that have to be
done**



JAN 03, 2016 DAY 8.5 Will see changes !



**Primer ON !
Cleanup Done**



OLD BAR !

JAN 04, 2016 DAY 9.5

FINISHING 1



JAN 04, 2016 DAY 9.5 FINISHING 2



Three Views

JAN 05, 2016 DAY 10.5 FINE TUNING




Its Coming together !



Light In, Ceiling Track
In, Cleanup,

JAN 06, 2016 DAY 11.5

FLOOR GOING IN

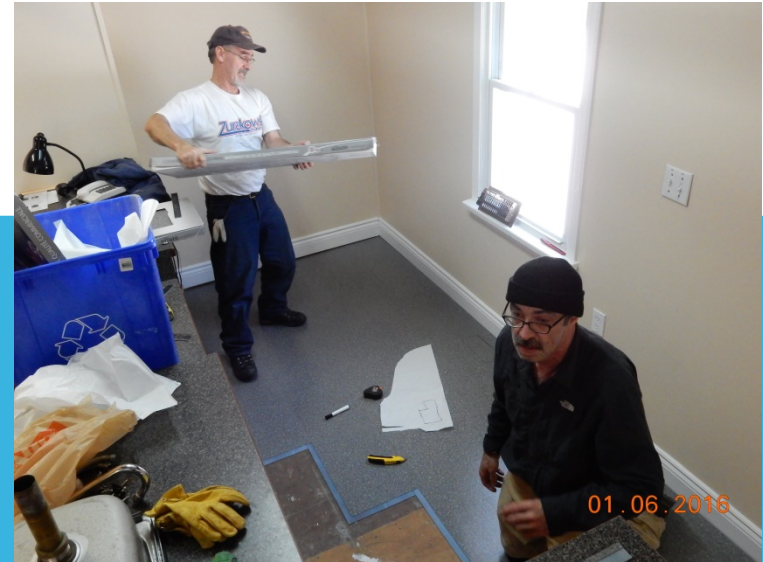

JAN 06, 2016 DAY 11.5


BAR VIEWS



AFTER 14 DAYS P1



AFTER 14 DAYS P2

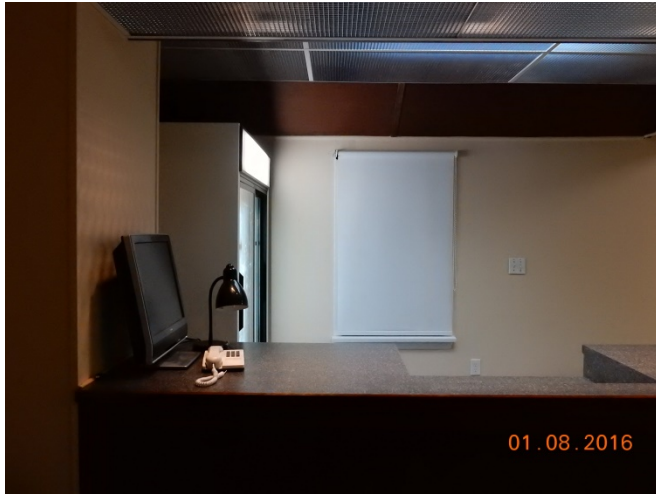

AFTER 14 DAYS P3 THAT'S IT – AFTER –



01.08.2016





Steve & Joe – Cleaning old Glue off



Clean – Ready for New



New Cut In //// Fred - Rolling New





We are Done



**THANKS TO ALL THE
CONSTRUCTION WORKERS**

Stan Gibbs

Steve Couture

Brian Ernteman

George Maudsley

Lawrence Lainchbury

Howard Pearcey

Luigi Liberator

Todd Stewart

Don Colburne

Wesley Lovell

David Jeffries

Fred Manuel

This will be the last last Update Feb 04, 2016
